



| ID | | % Work Complete | Notes | Task Name | Duration | Start | Finish | Predecessors | Resource Names | | | |
|----------------------------------------|---|-----------------|-------|-----------------------|-------------|--------------------|-------------|-----------------------|----------------|---|---|--|
| | | | | | | | | | | M | T | |
| 1 | ✓ | 100% | | Login | 2 days? | Wed 7/24/13 | Thu 7/25/13 | | | | | |
| 2 | ✓ | 100% | | Login facebook view | 1 day? | Wed 7/24/13 | Wed 7/24/13 | | | | | |
| 3 | ✓ | 100% | | LogOut | 1 day? | Thu 7/25/13 | Thu 7/25/13 | 2 | | | | |
| 4 | | 0% | | Settings | 3 days? | Thu 7/25/13 | Sat 7/27/13 | | | | | |
| 5 | ✓ | 100% | | Social Networks | 1 day? | Thu 7/25/13 | Thu 7/25/13 | 2 | | | | |
| 6 | ✓ | 100% | | Notification Settings | 1 day? | Fri 7/26/13 | Fri 7/26/13 | 5 | | | | |
| 7 | ✓ | 100% | | Privacy Settings | 1 day? | Fri 7/26/13 | Fri 7/26/13 | 5 | | | | |
| 8 | | 0% | | Contact TasteSync | 1 day? | Sat 7/27/13 | Sat 7/27/13 | 7 | | | | |
| 9 | 📅 | 0% | ? | Rate this App | 1 day? | Sat 7/27/13 | Sat 7/27/13 | 7 | | | | |
| 10 | | 0% | | About TasteSync | 1 day? | Sat 7/27/13 | Sat 7/27/13 | 7 | | | | |
| 11 | | 0% | | Profile | 3 days? | Mon 7/29/13 | Wed 7/31/13 | | | | | |
| 12 | | 0% | | Information | 1 day? | Mon 7/29/13 | Mon 7/29/13 | 10 | | | | |
| 13 | | 0% | | About | 1 day? | Mon 7/29/13 | Mon 7/29/13 | 10 | | | | |
| 14 | | 0% | | Number | 2 days? | Mon 7/29/13 | Tue 7/30/13 | | | | | |
| 15 | | 0% | | Show following | 1 day? | Mon 7/29/13 | Mon 7/29/13 | 10 | | | | |
| 16 | | 0% | | Show followers | 1 day? | Mon 7/29/13 | Mon 7/29/13 | 10 | | | | |
| 17 | | 0% | | Show friends | 1 day? | Tue 7/30/13 | Tue 7/30/13 | 16 | | | | |
| 18 | | 0% | | Restaurant | 2 days? | Tue 7/30/13 | Wed 7/31/13 | | | | | |
| 19 | | 0% | | Show list | 1 day? | Tue 7/30/13 | Tue 7/30/13 | 16 | | | | |
| 20 | | 0% | | Restaurant detail | 1 day? | Wed 7/31/13 | Wed 7/31/13 | 19 | | | | |
| 21 | | 0% | | Login sign up detail | 1 day? | Thu 8/1/13 | Thu 8/1/13 | 20 | | | | |
| | | | | | | | | | | | | |
| Project: UAT_Plan Date: Sat 7/27/13 | | | | Task | <div></div> | External Milestone | <div></div> | Manual Summary Rollup | <div></div> | | | |
| | | | | Split | <div></div> | Inactive Task | <div></div> | Manual Summary | <div></div> | | | |
| | | | | Milestone | <div></div> | Inactive Milestone | <div></div> | Start-only | <div></div> | | | |
| | | | | Summary | <div></div> | Inactive Summary | <div></div> | Finish-only | <div></div> | | | |
| | | | | Project Summary | <div></div> | Manual Task | <div></div> | Deadline | <div></div> | | | |
| | | | | External Tasks | <div></div> | Duration-only | <div></div> | Progress | <div></div> | | | |
| Page 1 | | | | | | | | | | | | |

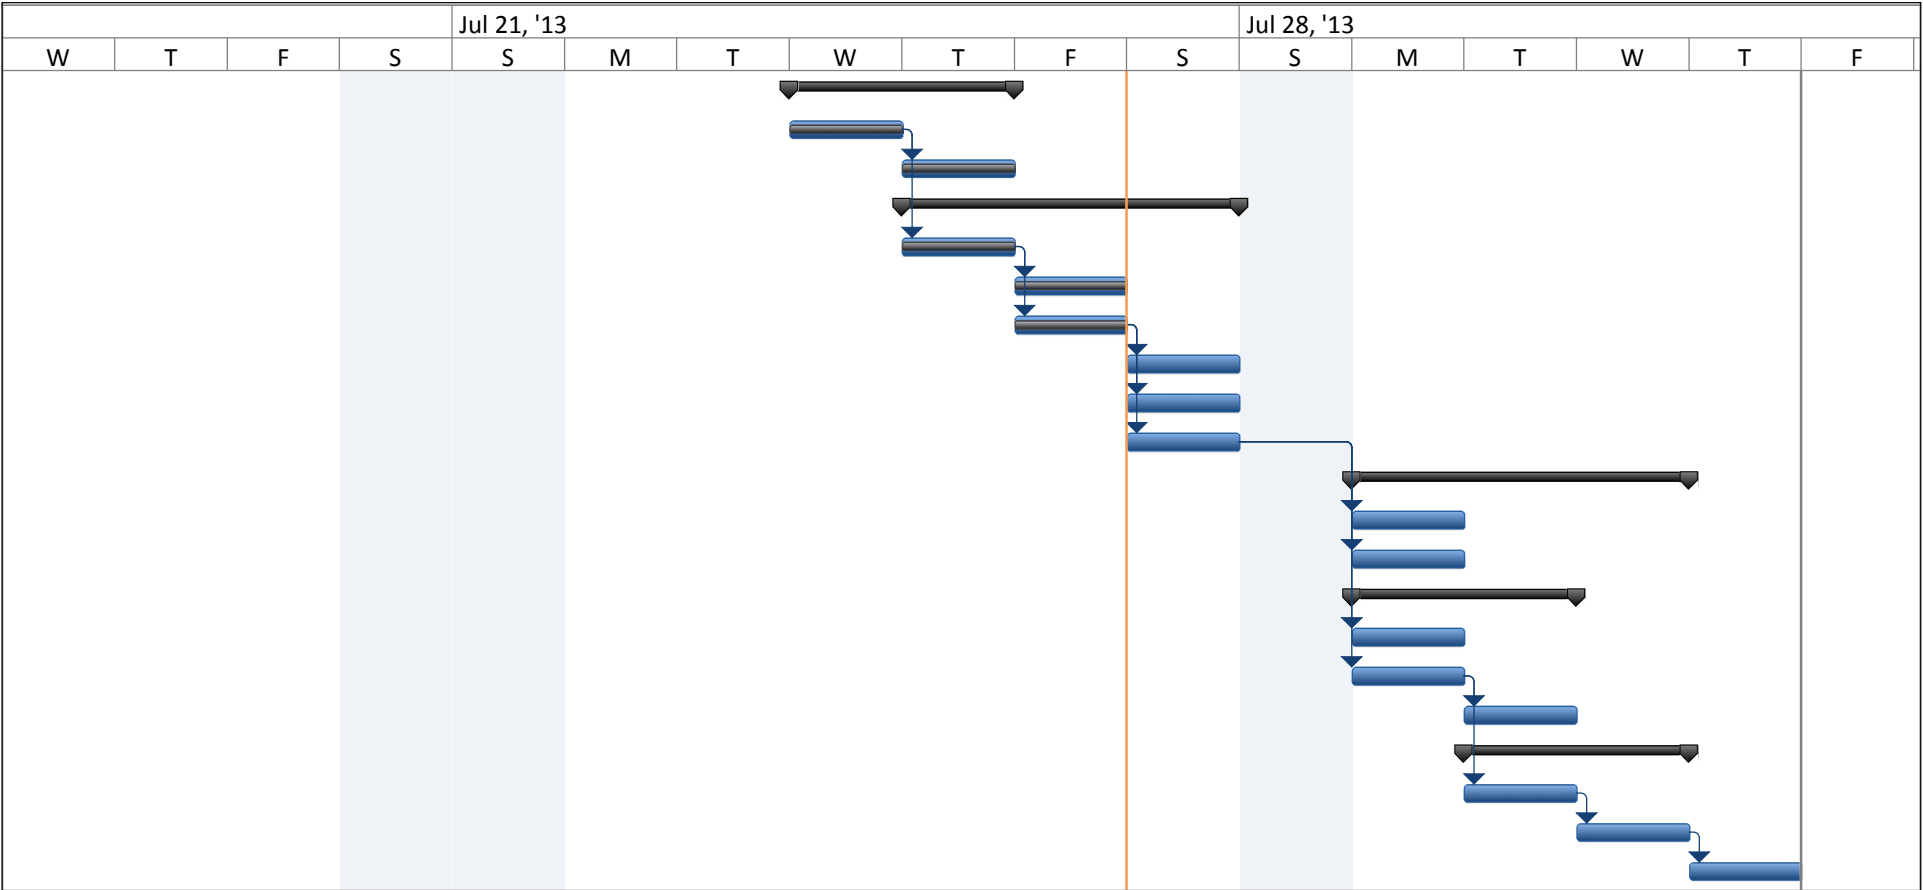

| | | | | | | |
|----------------------------------------|-----------------|--|--------------------|--|-----------------------|--|
| Project: UAT_Plan Date: Sat 7/27/13 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |
