ID		% Work Complete	Task Name	Duration	Start	Finish	Predec	Resource Names	13	
									M	T
1	✓	100%	submitSettingsNotifications + showSettingsNotifications	1 day	Wed 7/3/13	Wed 7/3/13		Rick Phan		
2	✓	100%	submitSettingsPrivacy + showSettingsPrivacy	1 day	Thu 7/4/13	Thu 7/4/13	1	Rick Phan		
3	✓	100%	submitSettingscontactUs + showAboutTastesync	1 day	Fri 7/5/13	Fri 7/5/13	2	Rick Phan		
4	✓	100%	submitMyProfileAboutMe+ showUserProfileFriend	1 day	Mon 7/8/13	Mon 7/8/13	3	Rick Phan		
5	✓	100%	showProfileFollower+ showProfileFollowing	1 day	Mon 7/8/13	Mon 7/8/13	3	Habbot Phan		
6	✓	100%	submitFollowUserStatusChange + showFollowStatus	1 day	Tue 7/9/13	Tue 7/9/13	5	Habbot Phan		
7	✓	100%	submitTrustedFriendStatusChange+ showTrustedFriend	1 day	Tue 7/9/13	Tue 7/9/13	4	Rick Phan		
8	✓	100%	sendMessageToUser+ showRestaurantSuggestion	1 day	Wed 7/10/13	Wed 7/10/13	7	Rick Phan		
9		50%	showMyProfileHome+ showProfileRestaurants	1 day	Wed 7/10/13	Wed 7/10/13	6	Habbot Phan		
10		0%	submitSignupDetail+ showSignupDetail	1 day	Thu 7/11/13	Thu 7/11/13	8	Rick Phan		
11		0%	inviteFriend+ submitUserReport	1 day	Thu 7/11/13	Thu 7/11/13	9	Habbot Phan		

Project: Plan
Date: Wed 7/10/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

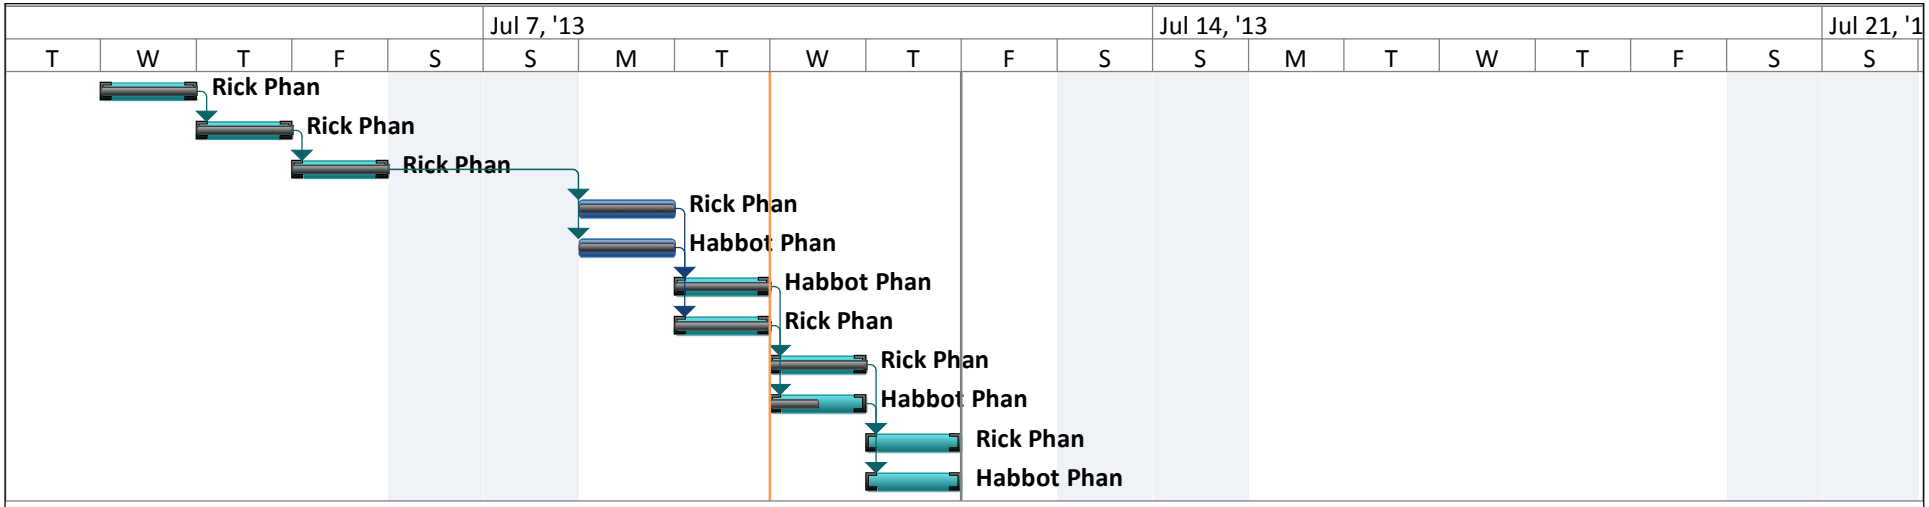

Project: Plan
Date: Wed 7/10/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	
